


National Currency Printing and Secure Banknote Production Facility Project (NCPBF)

(For learning purpose and homework)

Project Schedule

ID	Task Mode	Task Name	Duration	Predecessor	Start	Finish
0		Project Schedule _ Template _ PMIC	1544 days		Mon 2/1/27	Thu 12/30/32
1		Control Account 1.1	326 days		Mon 2/1/27	Mon 5/1/28
2		Start Control Account 1.1 Milestone	0 days		Mon 2/1/27	Mon 2/1/27
14		Charter Approval Milestone	0 days	13	Tue 6/1/27	Tue 6/1/27
24		Governance Framework Implementation Milestone	0 days	23	Tue 8/31/27	Tue 8/31/27
35		Schedule Baseline Approved Milestone	0 days	34	Mon 12/13/27	Mon 12/13/27
42		Cost Baseline Approved Milestone	0 days	41	Mon 3/6/28	Mon 3/6/28
49		Risk and Change Control Operational Milestone	0 days	43	Mon 3/20/28	Mon 3/20/28
54		Stage-Gate Reviews Milestone	0 days	49	Mon 3/20/28	Mon 3/20/28
59		Security Governance Milestone	0 days	57	Mon 3/27/28	Mon 3/27/28
63		Benefits Tracking Milestone	0 days	57	Mon 3/27/28	Mon 3/27/28
68		End Control Account 1.1 Milestone	0 days	67	Wed 4/19/28	Wed 4/19/28
69		Control Account 1.2	797 days		Wed 4/14/27	Fri 5/3/30
70		Start Control Account 1.2 Milestone	0 days	8	Wed 4/14/27	Wed 4/14/27
84		Site Preparation Complete Milestone	0 days	83	Mon 12/13/27	Mon 12/13/27
96		Facility Design Approval Milestone	0 days	95	Mon 7/24/28	Mon 7/24/28
106		Security Perimeter Construction Milestone	0 days	105	Fri 2/2/29	Fri 2/2/29
116		Structural Construction Milestone	0 days	115	Fri 5/25/29	Fri 5/25/29
123		Vault Construction Milestone	0 days	122	Thu 10/11/29	Thu 10/11/29
132		Construction Completion Milestone	0 days	131	Fri 5/3/30	Fri 5/3/30
133		End Control Account 1.2 Milestone	0 days	132	Fri 5/3/30	Fri 5/3/30
134		Control Account 1.3	760 days		Thu 4/5/29	Thu 3/4/32
135		Start Control Account 1.3 Milestone	0 days	111	Thu 4/5/29	Thu 4/5/29
152		Printing Press Contract Signed Milestone	0 days	151	Thu 1/3/30	Thu 1/3/30
157		Printing Press Procurement Package Milestone	0 days	156	Thu 11/21/30	Thu 11/21/30
164		Finishing Equipment Contract Award Milestone	0 days	163	Thu 2/6/31	Thu 2/6/31
175		Logistics Completion Milestone	0 days	174	Mon 6/2/31	Mon 6/2/31
185		Machinery Installation Complete	0 days	184	Mon 10/6/31	Mon 10/6/31
192		System Integration Testing Milestone	0 days	191	Fri 12/26/31	Fri 12/26/31
199		End Control Account 1.3	0 days	198	Thu 3/4/32	Thu 3/4/32
200		Control Account 1.4	123 days		Mon 10/6/31	Thu 3/25/32
201		Start Control Account 1.4	0 days	185	Mon 10/6/31	Mon 10/6/31
211		PMS Deployment Milestone	0 days	209	Wed 11/19/31	Wed 11/19/31
220		Inventory System Operational	0 days	218	Fri 1/16/32	Fri 1/16/32
227		RBAC System Operational	0 days	225	Thu 2/5/32	Thu 2/5/32
236		Monitoring Platform Operational	0 days	234	Wed 3/24/32	Wed 3/24/32
237		End Control Account 1.4	0 days	235	Thu 3/25/32	Thu 3/25/32
238		Control Account 1.5	155 days		Thu 3/4/32	Thu 10/7/32
239		Start Control Account 1.5	0 days	199	Thu 3/4/32	Thu 3/4/32
251		Access Control Operational	0 days	250	Wed 7/21/32	Wed 7/21/32

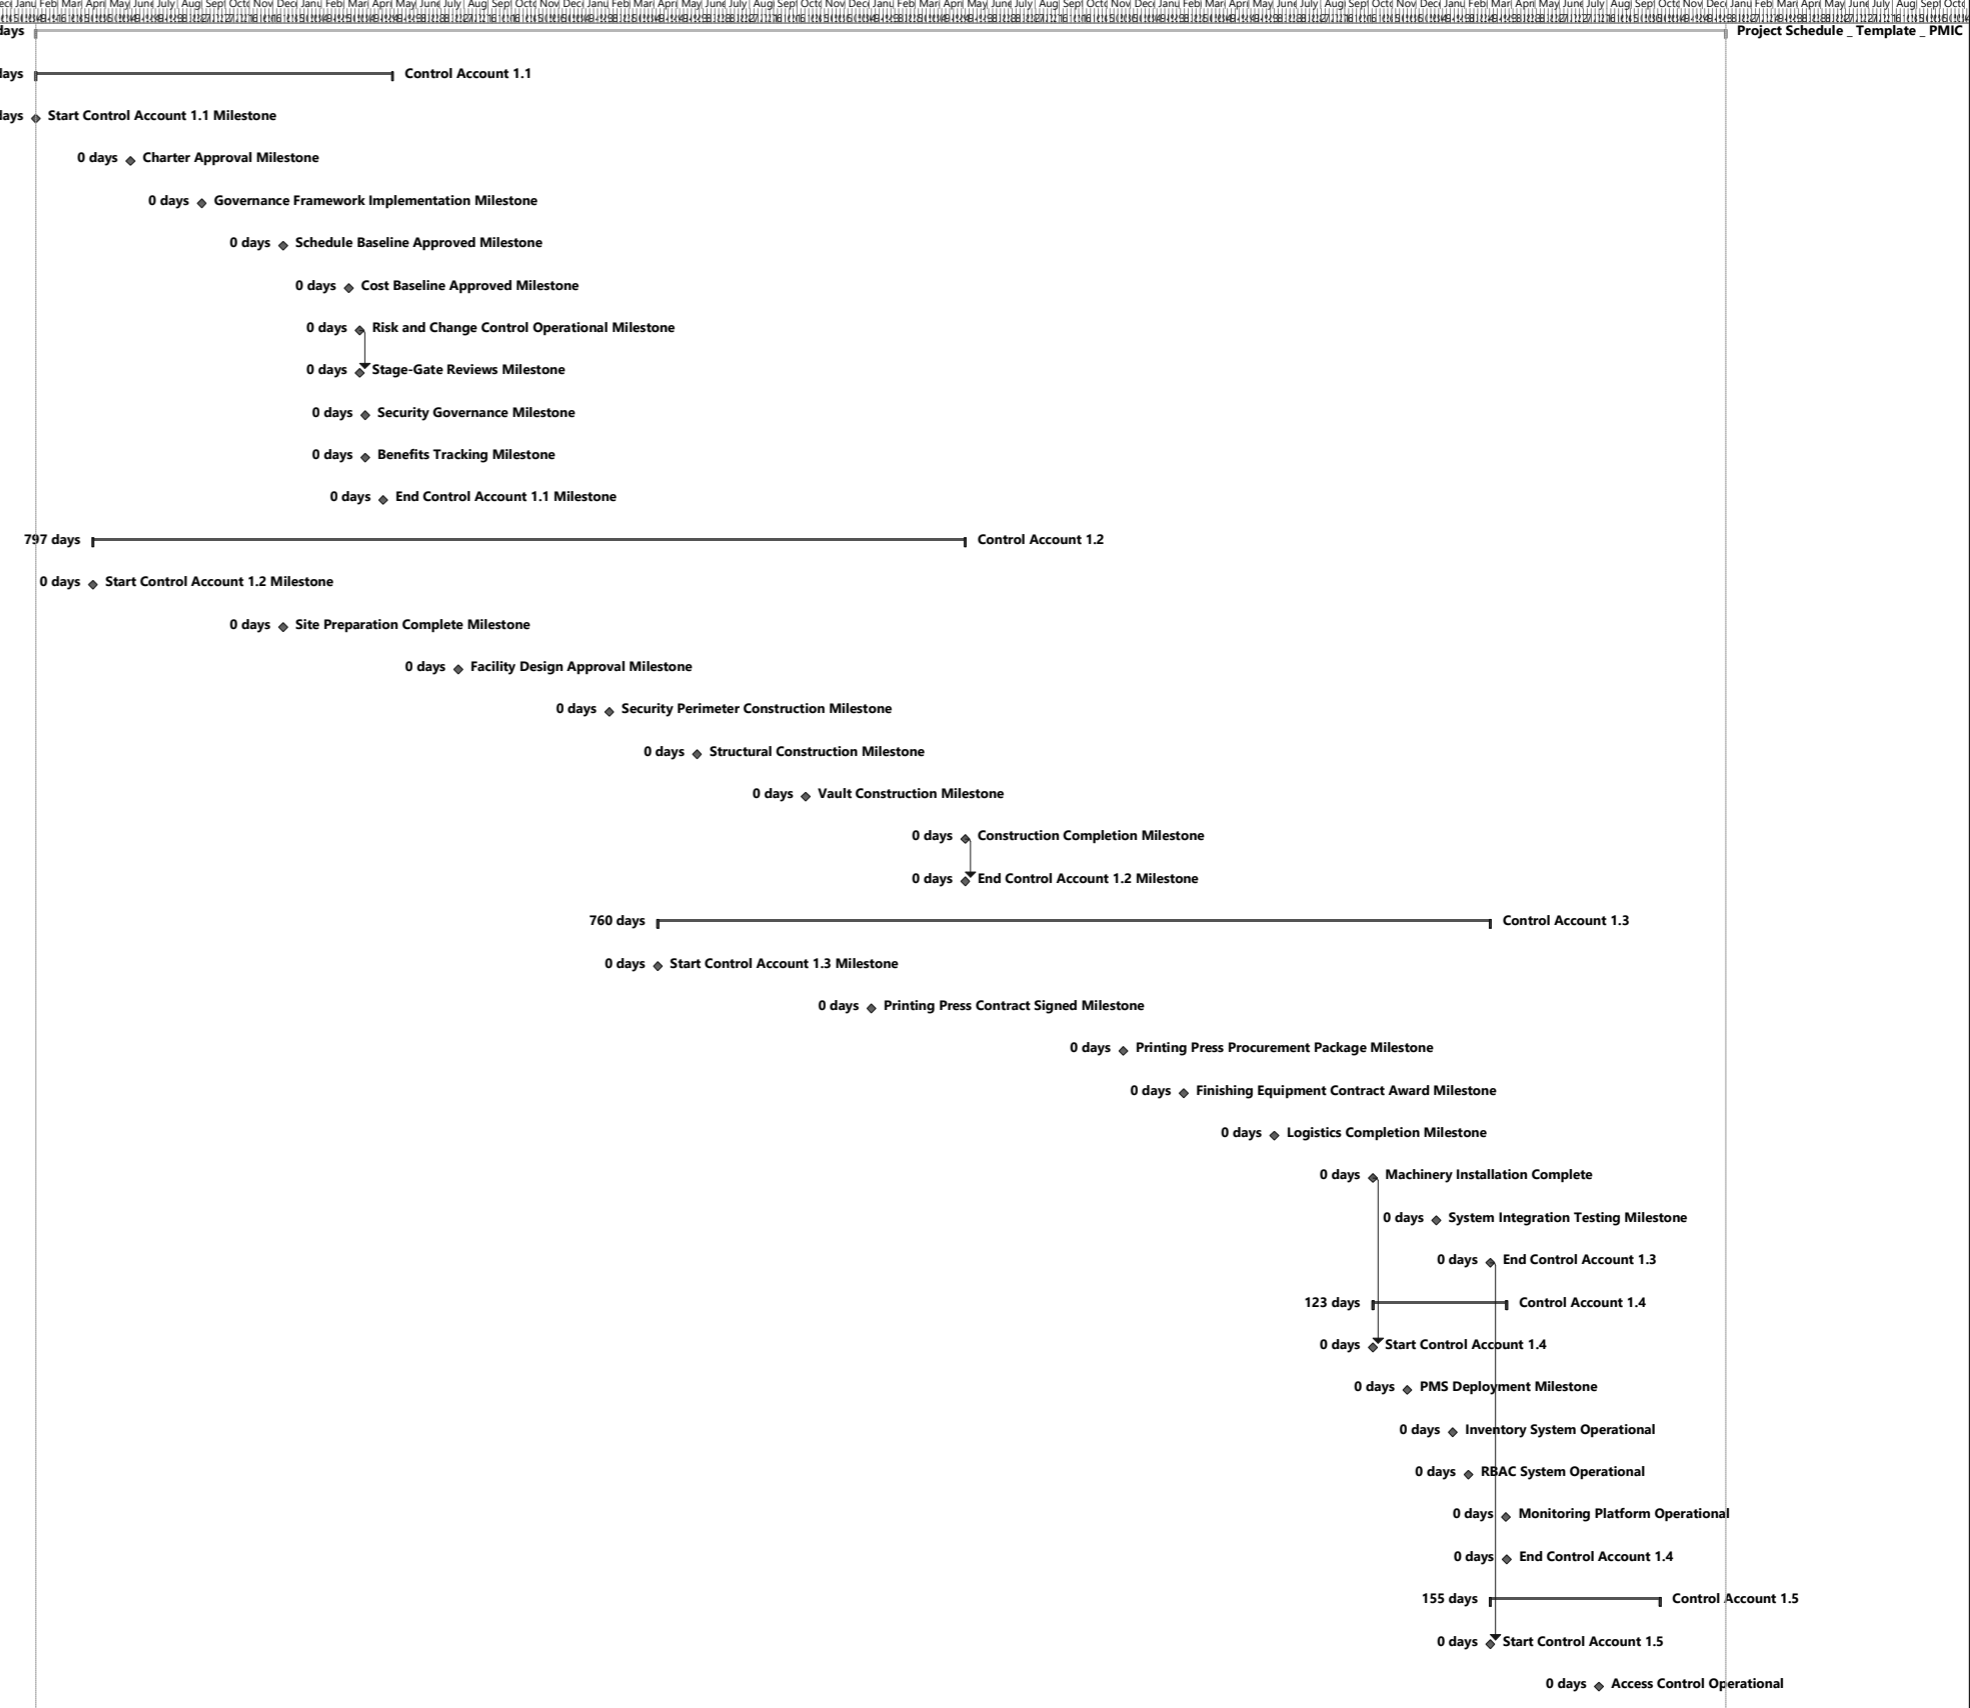

National Currency Printing and Secure Banknote Production Facility Project (NCPBF)

(For learning purpose and homework)

Project Schedule

ID	Task Mode	Task Name	Duration	Predecessor	Start	Finish
260		Biometric System Operational	0 days	259	Thu 10/7/32	Thu 10/7/32
261		End Control Account 1.5	0 days	260	Thu 10/7/32	Thu 10/7/32
262		Control Account 1.6	124 days		Thu 2/6/31	Wed 7/30/31
263		Start Control Account 1.6	0 days	163	Thu 2/6/31	Thu 2/6/31
274		FAT Completed	0 days	273	Wed 5/14/31	Wed 5/14/31
284		SAT Completed	0 days	283	Wed 7/30/31	Wed 7/30/31
285		End Control Account 1.6	0 days	284	Wed 7/30/31	Wed 7/30/31
286		Control Account 1.7	79 days		Fri 12/26/31	Thu 4/15/32
287		Start Control Account 1.7	0 days	191	Fri 12/26/31	Fri 12/26/31
298		Operator Training Completed	0 days	297	Thu 4/15/32	Thu 4/15/32
299		End Control Account 1.7	0 days	298	Thu 4/15/32	Thu 4/15/32
300		Control Account 1.8	60 days		Thu 10/7/32	Thu 12/30/32
301		Start Control Account 1.8	0 days	261	Thu 10/7/32	Thu 10/7/32
308		Operational Startup Milestone	0 days	307	Tue 11/16/32	Tue 11/16/32
315		Project Closure Milestone	0 days	314	Thu 12/30/32	Thu 12/30/32

